App. F. IX-4

Previous References.

1946-47
(Est.)

File No. 80-46
Serial Nos. 1, 2, 3, 4 5.

RECEIVED

Later References.

Est-2-47-87

GENERAL AND REVENUE SECRETARIAT

Serial Nos. Five.

Part B for Aug 47.

SUBJECT

Thuppadahalli and Gadimakunte Tank works.
Jagalur Taluk.

No. PW. 4851-3 dated 3.2.47

To The C.E. for Sanction.
" Comptr.
" Auditor PWD. } thro' FD.

Sanctions the continuance of the Sub Div. for — till the end of June 1948.

No. PW. 2317-19 dated 26.8.47.

To The C.E. for Sanction.
" Comptr.
" Auditor PWD } thro' FD.

Sanctions the formation of two Separate P.W. Sub Divisions for the execution of — —

Serial No.

Letter No 4335-7/E dated 17-2-1946 from the Chief Engineer for Irrigation.

Requests sanction to the Continuance of the Sub division Constituted for the execution of the Inpapadalli and Sokkehalla tank projects in Chitaldrug District, till the end of June 1948.

1 Asst Engineer
1 Graduate Overseer (now Surveyor)
4 Surveyors (now Sub Overseers)
2 Clerks
4 Peons
10% Conveyance allowance to the Offr and staff.

The Constitution of a sub division with the marginally noted establishments was sanctioned in G.O. No PW 6524-27 (N) dated 24-3-1944 for a period of two years for the execution of the Inpapadalli and Sokkehalla tank projects in Jagalur taluk. The amounts of the sanctioned estimates for the two works are Rs 3.64 lakhs and Rs 2.85 lakhs respectively.

2. It is reported that an outlay of Rs 88,062/- and Rs 68,821/- respectively have been incurred on the two works upto end of October 1946, leaving a balance of Rs 2,75,938/- and Rs 2,16,179/- respectively to be worked out. The CE, therefore, recommends that the sub division may be continued till the end of June 1948, by which time the works are expected to be completed.

3. Leaving March 1944, the total outlay incurred by the Sub division for a period

NOTE—Contn.-Sheet.

Continuance of the sub division Constituted for Imphal airport and Sokkelalla tank project.

File No. of 194 . | Public Works Secretariat

Serial No.

of 2 3/4 years ie from April 44 to end of October 1946, is Rs 1,50,883/- This works out to an average of Rs 5060/- per month which seems to be poor, especially in view of the fact that the sub division has been solely Constituted for these works.

4. The proposal of the CE is for orders with financial Concurrence.

5. Whether there is adequate 7/1/47 amount available out of the provision for establishments in the proper estimates to cover the Co on account of continuance of the establishments has not been intimated.

6. Whether there is provision or not it is 2/1/47 necessary to Continue the sub divisio as proposed by the chief Engineer to work out the heavy balance of works still to be done. No doubt the progress of work is rather poor for the period of 2 3/4 years The proposal to Continue the establish ments upto June 1948 may be sanctio with strict instructions to complete the w by them.

Secy) 8 6/1/47

7. Sanction was accorded by Government

Continuance of the Sub division Constructed for the Thuppadahalla and Sokkehalla tank projects.

Public Works Secretariat | File No. | of 194 | [App. F. III–2

Serial No.

under order, for the constitution of the Sub Division for the execution of Tuppadahally and Sokkehalla Tank works in Chitaldroog District, for a period of two years. The period is over. The Chief Engineer reports that there is heavy balance of works to be done namely 2.76 lakhs in Tuppadahally project, against the sanctioned amount of 3.64 lakhs. and 2 lakhs in in Sakkenhally Tank work against the sanctioned amount of 2.85 lakhs i.e. there is still nearly 5 lakhs to be worked from both the tanks. He recommends the continuance of the Sub Division for a period of 3 till the end of June 1948. The Chief Engineer does not state why the progress was poor. As stated already, the amount of work to be executed still is Rs 5 lakhs. He has worked out, the progress per year for a sub Division can be Rs 2 lakhs a year. Hence the period as fixed by the Chief may be approved may be extended, now alone up to the end of Dec 48 as the Chief Engineer himself is doubtful about the period and states that the period may be extended up to the end of June 48 in the first instance. Hence the establishment may be continued up to the end of Dec 48. and the action taken by C.E in continuing the establishment beyond the sanctioned period, may be approved. The Chief Engineer for Irrigation

NOTE—Contn. Sheet:

Continuance of the sub-division construction Thippadahally and Sokkelalla projects

File No. | of 194 . | Public Works Secretariat

Serial No.

be continued that no retrenchment of time be permitted and that works shall be closed, and work finally accounted for in the period.

20 JAN NO. 5109

FINANCIAL U.O.No. 4736 1946 10/1 BANGALORE

Minister P.W.D and Diwan through the financial Secy

OFFICE OF THE MINISTER FOR AGRICULTURE AND PUBLIC WORKS 15 JAN. 1947 No. Camp-7

Progress is very poor. The C.E. should be requested to investigate into causes for this poor progress. I think constant supervision over these works is very necessary. The C.E. may hold up the officers in charge of these works. He may also see that they are given all facilities to enable them to get through the work. In the circumstances reported the proposal of the C.E. to continue the sub-division till the end of June 1948 may be sanctioned.

Diwan

10. Approved

Continuance of the Thuppadahalli & Gattimaranoor Tank Works Sub Dn

Public Works Secretariat | File No. of 194 . 3143 [illegible] App. F. III-2

Serial No.	
	13. Subd. with a draft G.O. and a letter 24/6/47. 24/6/47
	Fl. common No. 32.61.
	15. F/S. was agreed. Draft G.O. for Subd. 16. Done 5/7 Rly 6-7 [illegible] 6/7
	[illegible]
	Issued (i) G.O. No. P.W. 4851-3/Est 80-46-2 dated 3.7.47 To The C.E. for Irrigation The Comptroller to Govt The Audit & Pw Depts Thro' the usual
	Sanctions the continuance of the sub-division till the end of June 1948
	(ii) Letter No. PW 4854/Est-80-46-3 dated 3-7-47 To The C.E. for Irrigation
	Calls for a report on the progress secured on the Works.
	Letter No. 8583/E dated 29.5.1947 from the Chief Engineer for Irrigation forwarding a report on the above progress secured on the Works.
	17. Submitted with reference to the minute dated 17.1.1947 of the Minister for Agriculture in para 9 of the notes.

NOTE—Contn. Sheet.

43 U 6519

Embankment of the Sub division Comilla for Kadimakunte and Lobbakalla tanks project.

File No. of 194 . | Public Works Secretariat

Serial No.

18. The Chief reason for the short progress is stated to be paucity of pieceworkers and labour for excavation, want of carts for conveyance of materials to the tank sites and the inability of the Asst Engineer to supervise both the tank works effectively To secure better progress, the CE recommends the following two proposals:

(i) Formation of a new sub division in addition to the existing one with the establishment as shown in the proposal statement till the end of June 1948. This proposal, it is effect, will be to have an independent sub division for each work and (ii) The employment of 9 lorries with a quota of 150 gallons of petrol for each lorry per month.

19. The proposal now involves an extra cost of Rs 7,734/- per annum and constitutes Council matter. Financial Concurrence is also necessary.

20. Para 18 is for perusal with reference to para 9 supra.

21. Heavy balance of work being still to be done, viz, about 5.0 lakhs calls for increasing the establishment and facilities for speedy completion of the works.

22. The recommendations of the C.E.D. to the formation of an additional Sub Division till the end of June 1948 may perhaps be approved and sanctions accorded.

Secy.) HPS 17.6.47

Continuance of the Special Sub-Division constituted for the execution of Thuppadahally and Gadimakunte Tank Works in Dodaballapur Taluk.

Public Works Secretariat | File No. 6519 of 194 . | [App. F. III-2

Serial No. 23.

The Continuance of one Sub Division for Gadimakunte and Tuppadahally Tank Works, is Sanctioned till the end of June 48. In para 9, the Chief Engineer for Irrigation was requested to investigate the Cause of Slow progress etc. He explained the Causes as noted in para 18 and recommends the formation of Separate Sub Divisions for each of the tank works to speed up the progress and with the staff noted in the proposition Statement involving an excess of 7734. In the circumstances the Chief Engineer's proposal to have two Sub Divisions, one for each work may be Sanctioned till the end of June 1948. This is a Schedule case and may be disposed off by circulation

Min for Ag and P.W
and
Dewan
through Fin Secy

Posy 18-6-47

HPS
18-6-47

19-6-47.

Posy 20-6-47

HPS
20-6-47

OFFICE OF THE MINISTER FOR AGRICULTURE AND PUBLIC WORKS
21 JUNE 1947
No. 9738

G.O. No. 8743 19/6 BANGALORE

24. Construction of a tank near Tuppadahalli and another at Gadimakunte ~~were~~ was sanctioned by Government at an estimated cost of Rs. 3,64,000/- and Rs.2,85,000/ respectively. While sending up estimates for sanction of Government, the Chief ~~Elextr~~ Engineer for Irrigation had proposed two separate Sub Divisions

NOTE—Contn. Sheet.

Continuance of Special Sub Div for Thoppadakallu and Gadimaranka Irrigation works in Tanjore Dist

File No. of 194 . | Public Works Secretariat

Serial No. 9738

to be in charge of each work. Government, however sanctioned only one Sub Division observing that as the two works are in one and the same taluk one Sub Division would be sufficient. The progress in both the works has been very poor. In fact, up to the end of October 1946, an outlay of Rs. 88,062/- and Rs. 68,821/- has been incurred leaving a heavy balance of Rs. 2,75,938/- and Rs. 2,16,179/- respectively to be worked ~~out~~. When I visited these two works in January, I observed that the progress was very poor and that all efforts must be made to achieve proper progress. The Chief Engineer for Irrigation was later requested to investigate into the causes for poor progress and send up his proposals to Government for achieving more satisfactory progress. He has accordingly sent up a proposal to sanction one more Sub Division with the necessary staff, so that each work may be in charge of an independant Sub Division. Though both the works are in one taluk, the distance between the places is very nearly 30 miles and it is not possible for one Assistant Engineer to effectively supervise the works. In the circumstances, sanction may be accorded to the proposal of the Chief Engineer for Irrigation.

25. But, the establishment of Sub Division is not in itself sufficient. I know gravel and kankar have to be transported from a distance to the work-spot. Unless adequate facilities by way of lorries and petrol is given, I do not think it is possible to show any appreciable progress in these works. The Chief Engineer for Irrigation may be requested to afford them the necessary transport facilities.

26. This is a Council matter. 27. 28. circulate

Dewan) 29.

Continuance of the Special Sub-division for Irrigation and Cardamom Farm Works in Tafalur Taluk.

Continuation Sheet. File No. Current No. Page. 651 9

30. Subd with a circulation note

B 30/6/47. Minister for Agri. & P.W. Bm 1/7/47

for approval

HPS 1.7.47

Copies of circulation notes are put up.

B 7/7/47. Chief Secretary wrote Compote Bm 8/7/47

HPS 8.7.47

OFFICE OF THE MINISTER FOR AGRICULTURE AND PUBLIC WORKS 7 JULY 1947 No. 67

225

CHIEF SECRETARY 11 JUL 1947 GOVT. OF MYSORE

OFFICE OF THE MINISTER FOR AGRICULTURE AND PUBLIC WORKS 1 AUG. 1947 No. 1008

Council File No. 60 d 15 FOR DISPOSAL BY CIRCULATION. WQ 7/7/47

Views of the Ministers are placed below

Secretary to Government

.....P.W.....Dept.

with compliments WQ 26/7/47

8. AUG. 1947 1090

Put up D.F.N

Subd with a draft final note. Bm 28.7.47

HPS 28.7.47

B 30/7/47. Ministers for Agri. & P.W.

30/7/47 final Note placed below Bm 31/7 HPS 30.7.47

Dewan/Bm 7.8.47

AA 199

Note for circulation

Proposal

Two Separate Public Works Sub divisions for the execution of Thuppadahalli and Gadimakunte Tank Works in Jagalur Taluk

Two estimates amounting to Rs 3.66 Lakhs and Rs 2.85 Lakhs were sanctioned in March 1946 for the Construction of tanks near Thuppadahalli and Gadimakunte respectively in Jagalur taluk. At the time of sanctioning these estimates the Chief Engineer proposed the formation of two separate sub divisions for the execution of these two tank works However only one sub division was sanctioned as Govt considered that the two works are in one and the same taluk and that one sub division would be sufficient. The sanction accorded in Feb 47 to the Continuance of this sub division as it is by the end of June 1948.

When the Minister for Agri & PW visited the works in January last, he was observed that the progress on these work was very poor. Upto end of Octobr 1946, an outlay of Rs 88,062/- and Rs 68,821/- had been incurred leaving a heavy balance of Rs 2,75,938/- and Rs 2,16,179/- respectively. The Chief Engineer for Irrigation who was requested to investigate

with the cause for poor progress, has forwarded proposals for the formation of one more sub division with the necessary staff, till the end of June 1948 so that each work may be in independent charge of each sub division. Though the works are in one taluk, the distance between the places is very nearly 30 miles and it is not possible for one Asst Engr to effectively supervise the work. The extra cost involved is Rs 7,734/- per annum. In these circumstances, the proposal of the Chief Engineer has been approved by the Dewan and the Minister for PW and concurred in by the Financial Secretary. The concurrence of the other Ministers is required before submission to H.H. for sanction.

This is for disposal by circulation

30/6/47

HPS 1.7.47

Bn 1/7/47

Approved HH 3/7/47

Bn 3.7.47

HPS 4.7.47

Council File No. 60 d/5/7
FOR DISPOSAL BY CIRCULATION
Chief Edn.

Note for Circulation.

Subject:- Proposal to form two separate Public Works Sub Divisions for the Execution of Thuppadahalli and Gadimakunte tank works in Jagalur Taluk.

Two estimates amounting to Rs.3.64 lakhs and Rs.2.85 lakhs were sanctioned in March 1944 for the construction of tanks near Thuppadahalli and Gadimakunte respectively in Jagalur Taluk. At the time of sanctioning these estimates, the Chief Engineer proposed the formation of two separate Sub Divisions for the execution of these two tank works. However, only one Sub Division was sanctioned as Government considered that the two works are in one and the same taluk and that one Sub Division would be sufficient. The sanction accorded in February 1947 to the continuance of this Sub Division expires by the end of June 1948.

When the Minister for Agriculture & Public Works visited the works in January last, he observed that the progress on these works was very poor. In fact up to end of October 1946, an outlay of Rs.83,062/- and Rs.68,821/- had been incurred leaving a heavy balance of Rs.2,75,938/- and Rs.2,16,173/- respectively. The Chief Engineer for Irrigation, who was requested to investigate into the causes for poor progress, has forwarded proposals for the formation of one more sub division with the necessary staff till the end of June 1948, so that each work may be in independant charge of each sub division officer. Though both the works are in one taluk, the distance between the places is very nearly 30 miles and it is not possible for one Asst. Engineer to effectively supervise the works. The extra cost involved is Rs.7,734/- per annum.

In these circumstances, the proposal of the Chief Engineer has been approved by the Dewan and Minister for Public Works and concurred in by the Financial Secretary. The concurrence of the other Ministers is required before submission to His Highness for sanction.

This is for disposal by circulati

Council File No. 600 d 1/22
FOR DISPOSAL BY CIRCULATION
Min Law

Note for Circulation.

Subject:- Porposal to form two separate Public Works Sub Divisions for the Execution of Thuppadahalli and Gadimakunte tank works in Jagalur Taluk.

OFFICE OF THE MINISTER FOR LAW
No. 513

Two estimates amounting to Rs.3.64 lakhs and Rs.2.85 lakhs were sanctioned in March 1944 for the construction of tanks near Thuppadahalli and Gadimakunte respectively in Jagalur Taluk. At the time of sanctioning these estimates, the Chief Engineer proposed the formation of two separate Sub Divisions for the execution of these two tank works. However only one Sub Division was sanctioned as Government considered that the two works are in one and the same taluk and that one Sub Division would be sufficient. The sanction accorded in February 1947 to the continuance of this Sub Division expires by the end of June 1948.

When the Minister for Agriculture & Public Works visited the works in January last, he observed that the progress on these works was very poor. In fact up to end of October 1946, an outlay of Rs.88,062/- and Rs.68,821/- had been incurred leaving a heavy balance of Rs.2,75,938/- and Rs.2,16,179/- respectively. The Chief Engineer for Irrigation, who was requested to investigate into the causes for poor progress, has forwarded proposals for the formation of one more sub division with the necessary staff, till the end of June 1948, so that each work may be in independent charge of each sub division officer. Though both the works are in one taluk, the distance between the places is very nearly 30 miles and it is not possible for one Asst. Engineer to effectively supervise the works. The extra cost involved is Rs.7,734/- per annum.

In these circumstances, the proposal of the Chief Engineer has been approved by the Dewan and Minister for Public Works and concurred in by the Finanacial Secretary. The concurrence of the other Ministers is required before submission to His Highness for sanction.

This is for disposal by circulation.

1394/8 2/47

Council File No. G.O.d 157
FOR DISPOSAL BY CIRCULATION.

OFFICE OF THE MINISTER FOR AGRICULTURE AND PUBLIC WORKS
15 JULY 1947
No. 282

Note for Circulation.

Subject:- Porposal to form two separate Public Works Sub-Divisions for the Execution of Thuppadahalli and Gadimakunte tank works in Jagalur Taluk.

Two estimates amounting to Rs.3.64 lakhs and Rs.2.85 lakhs were sanctioned in March 1944 for the construction of tanks near Thuppadahalli and Gadimakunte respectively in Jagalur Taluk. At the time of sanctioning these estimates, the Chief Engineer proposed the formation of two separate Sub Divisions for the execution of these two tank works. However, only one Sub Division was sanctioned as Government considered that the two works are in one and the same taluk and that one Sub Division would be sufficient. The sanction accorded in February 1947 to the continuance of this Sub Division expires by the end of June 1948.

When the Minister for Agriculture & Public Works visited the works in January last, he observed that the progress on these works was very poor. In fact up to end of October 1946, an outlay of Rs.88,062/- and Rs.68,821/- had been incurred leaving a heavy balance of Rs.2,75,938/- and Rs.2,16,179/- respectively. The Chief Engineer for Irrigation, who was requested to investigate into the causes for poor progress, has forwarded proposals for the formation of one more sub division with the necessary staff, till the end of June 1948, so that each work may be in independent charge of each sub division officer. Though both the works are in one taluk, the distance between the places is very nearly 30 miles and it is not possible for one Asst. Engineer to effectively supervise the works. The extra cost involved is Rs.7.734/- per annum.

In these circumstances, the proposal of the Chief Engineer has been approved by the Dewan and Minister for Public Works and concurred in by the Financial Secretary. The concurrence of the other Ministers is required before submission to His Highness for sanction.

This is for disposal by circulation.

Council File No. 60 d 157

FOR DISPOSAL BY CIRCULATION

Their Highnesses

Note for Circulation

Subject:- Proposal to form two separate Public Works Sub Divisions for the Execution of Thuppadahalli and Gadimakunte tank works in Jagalur Taluk.

Two estimates amounting to Rs.3.64 lakhs and Rs.2.85 lakhs were sanctioned in March 1944 for the construction of tanks near Thuppadahalli and Gadimakunte respectively in Jagalur Taluk. At the time of sanctioning these estimates, the Chief Engineer proposed the formation of two separate Sub Divisions for the execution of these two tank works. However, only one Sub Division was sanctioned as Government considered that the two works are in one and the same taluk and that one Sub Division would be sufficient. The sanction accorded in February 1947 to the continuance of this Sub Division expires by the end of June 1948.

When the Minister for Agriculture & Public Works visited the works in January last, he observed that the progress on these works was very poor. In fact up to end of October 1946 an outlay of Rs.80,062/- and Rs.68,621/- had been incurred leaving a heavy balance of Rs.2,75,938/- and Rs.2,16,170/- respectively. The Chief Engineer for Irrigation, who was requested to investigate into the causes for poor progress, has forwarded proposals for the formation of one more sub division with the necessary staff, till the end of June 1948, so that each work may be in independent charge of each sub division officer. Though both the works are in one taluk, the distance between the places is very nearly 30 miles and it is not possible for one Asst. Engineer to effectively supervise the works. The extra cost involved is Rs.7,734/- per annum.

In these circumstances, the proposal of the Chief Engineer has been approved by the Dewan and Minister for Public Works and concurred in by the Financial Secretary. The concurrence of the other Ministers is required before submission to His Highness for sanction.

This is for disposal by circulation.

Bng/8-2-47

Council No. 60 d 1/7
FOR DISPOSAL BY CIRCULATION

Note for Circulation.

Subject:- Proposal to form two separate Public Works Sub Divisions for the Execution of Thuppadahalli and Gadimakunte tank works in Jagalur taluk.

OFFICE OF THE MINISTER FOR REVENUE
No. 431
Date 15-7-1947

Two estimates amounting to Rs.3.64 lakhs and Rs.2.85 lakhs were sanctioned in March 1944 for the construction of tanks near Thuppadahalli and Gadimakunte respectively in Jagalur Taluk. At the time of sanctioning these estimates, the Chief Engineer proposed the formation of two separate Sub Divisions for the execution of these two tank works. However only one Sub Division was sanctioned as Government considered that the two works are in one and the same taluk and that one Sub Division would be sufficient. The sanction accorded in February 1947 to the continuance of this Sub Division expires by the end of June 1948.

No remarks

When the Minister for Agriculture & Public Works visited the works in January last, he observed that the progress on these works was very poor. In fact up to end of October 1946, an outlay of Rs.88,062/- and Rs.68,821/- had been incurred leaving a heavy balance of Rs.2,75,938/- and Rs.2,16,179/- respectively. The Chief Engineer for Irrigation, who was requested to investigate into the causes for poor progress, has forwarded proposals for the formation of one more sub division with the necessary staff, till the end of June 1948, so that each work may be in independent charge of each sub division officer. Though both the works are in one taluk, the distance between the places is very nearly 30 miles and it is not possible for one Asst. Engineer to effectively supervise the works. The extra cost involved is Rs.7.734/- per annum.

In these circumstances, the proposal of the Chief Engineer has been approved by the Dewan and Minister for Public Works and concurred in by the Financial Secretary. The concurrence of the other Ministers is required before submission to His Highness for sanction.

This is for disposal by circulation.

Bangalore 1/7

Cabinet File No 6 o d 137
FOR DISPOSAL & CIRCULATION.

Note for Circulation.

Subject:- Proposal to form two separate Public Works Sub Divisions for the Execution of Thuppadahalli and Gadimakunte tank works in Jagalur Taluk.

Two estimates amounting to Rs.3.64 lakhs and Rs.2.85 lakhs were sanctioned in March 1944 for the construction of tanks near Thuppadahalli and Gadimakunte respectively in Jagalur Taluk. At the time of sanctioning these estimates, the Chief Engineer proposed the formation of two separate Sub Divisions for the execution of these two tank works. However only one Sub Division was sanctioned as Government considered that the two works are in one and the same taluk and that one Sub Division would be sufficient. The sanction accorded in February 1944 to the continuance of this Sub Division expires by the end of June 1948.

When the Minister for Agriculture & Public Works visited the works in January last, he observed that the progress on these works was very poor. In fact up to end of October 1946, an outlay of Rs.88,065/- and Rs.69,821/- had been incurred leaving a heavy balance of Rs.2,75,938/- and Rs.2,16,179/- respectively. The Chief Engineer for Irrigation, who was requested to investigate into the causes for poor progress, has forwarded proposals for the formation of one more sub division with the necessary staff, till the end of June 1948, so that each work may be in independent charge of each sub division officer. Though both the works are in one taluk, the distance between the places is very nearly 30 miles and it is not possible for one Asst. Engineer to effectively supervise the works. The extra cost involved is Rs.7,734/- per annum.

In these circumstances, the proposal of the Chief Engineer has been approved by the Dewan and Minister for Public Works and concurred in by the Financial Secretary. The concurrence of the other Ministers is required before submission to His Highness for sanction.

This is for disposal by circulation.

Bng 8/47

Final Note by the Minister for Agriculture and Public Works.

Subject.— Proposal to form two separate Public Works Sub Divisions for the execution of Thuppadahalli and Gadimakunte tank works in Jagalur taluk.

'A' Two estimates amounting to Rs. 3.64 lakhs and Rs. 2.85 lakhs were sanctioned in March 1944 for the construction of tanks near Thuppadahalli and Gadimakunte respectively in Jagalur taluk. At the time of sanctioning those estimates, the Chief Engineer proposed the formation of two separate Sub Divisions for the execution of these two tank works. However, only one Sub Division was sanctioned, as Government considered that the two works are in one and the same taluk and that one Sub Division would be sufficient. 'C' The sanction accorded in February 1947 to the continuance of this Sub Division expires by the end of June 1948.

When the Minister for Agriculture and Public Works visited the works in January last, he observed that the progress on these works was very poor. In fact, up to end of October 1946, an outlay of Rs. 88,062/- and Rs. 68,821/- had been incurred leaving a heavy balance of Rs. 2,75,938/- and Rs. 2,16,179/- respectively. 'B' The Chief Engineer for Irrigation, who was requested to investigate into the causes for poor progress, has forwarded proposals for the formation of one more Sub Division with the necessary staff, till the end of June 1948, so that each work may be in independant charge of each Sub Division Officer. Though both the works are in one taluk, the distance between the places is very nearly 30 miles and it is not possible for one Assistant Engineer to effectively supervise the works. J The extra cost involved is Rs. 7,734/- per annum.

In these circumstances, the proposal of the Chief Engineer has been agreed to by the Dewan and the other Ministers. Para 28 of the 'Rules and Regs' I solicit the gracious sanction of His Highness thereto.

L. Siddappa

Bangalore,
4th August 1947.

Minister for Agriculture
and Public Works.

Submitted to His Highness.

I submit herewith a Final Note by the Minister for Agriculture and Public Works on the proposal to form two separate Public Works Sub Divisions for the execution of Thuppadahalli and Gadimakunte tank works in Jagalur Taluk, for the gracious approval of His Highness.

Ramaswami Mudali

D E W A N.

Bangalore,
8th August 1947.

Record of Cases submitted for the Orders of His Highness the Maharaja.

Subject.

Proposal to form two separate Public Works Sub Division for the execution of Thuppadahalli and Gadimakunte tank works in Jagalur Taluk.

Rw.199

Order.

11/8/47.

Chief Secy

HRH
12/8

12/8

C 60

General and Revenue
Secretariat.

WD 06911—GPB—1000—3-7-47

SUBJECT :—

'Proposal to form two separate Public Works Sub Divisions for the execution of Tuppadahalli and Gadikunte tank works in Jagalur Taluk

65-19 P.W.

Issue and circulate.
P.W. / 13-8-47
HPS 13-8-47

Circulated to the Council of Ministers for perusal of His Highness' orders before/after issue of orders.

Sent with a draft
Issue
HPS 19-8-47
18/8/47 19-8-47

Chief Secretary to Government.
12/8

Through the Secretary to Government,
Public Works ...Department.

Fin-Com 9-8-0.
Fin Secretary agreed 16/8
Draft and Fair returned 1/9/47
Issue.
E-I/A 27/8

1. Minister for Education and Public Health. HPS 1/9/47

1515 2-9-47 2. Minister for Law. 2/9/47.

1794 30/8/47 3. Minister for Agriculture and Public Works. 30.8.47.

Issued

Issued P.W. 2317-19/6-C 28/8
80-46-S dt 26-8-47

1/26 1-9-47 4. Minister for Home. 1/9/47

CB.) 30-8-47

2507 1-9-47 5. Minister for Revenue and Communications. 1/9/47

Secretary to Government,
P.W. Department
(with compliments)

NOTE.—Contn. sheet

HPS 3/9/47 3-9-47 2/9/47

Gmt-80-46—1

No. 4335-7/E

Office of the Chief Engineer for
Irrigation in Mysore,
Dated Bangalore, 16th December 1946.

17/12

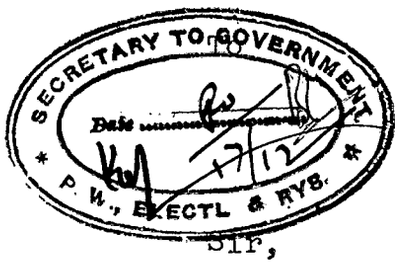

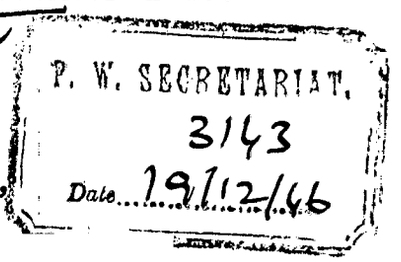

The Secretary to Government,
Public Works Department,
Bangalore.

Sir,

Continuance of the Special Sub Division for Thuppadahalli and Gadimakunte Tank works.

I have the honour to state that in Government Order No.P.W. 6524-28/Ext. 24-3-1944, sanction was accorded to the constitution of a Sub Division for a period of two years for the execution of the Thuppadahalli and Sokkehalla projects.

2. An outlay of Rs.88,062/- is reported to have been incurred on Thuppadahalli Project to the end of October 1946 against the sanctioned amount of Rs.3,64,000/- leaving a balance of Rs.2.76 lakh still to be worked out. It is reported that materials, such as gravel and stone required for puddle corewall embankment and revetment are being collected and 400 labourers are employed now on this work.

3. An outlay of Rs.68,821/- is reported to have been incurred to end of October 1946, on Sokkehalla Project against the sanctioned amount of Rs.2.85 lakhs. There is still more than 2 lakhs to be worked out. Earthwork in the portion ~~of~~ adjoining valley is under progress. Bank in grades 18 to 31 is being raised in the rear. The puddle breach filling in grades 18 to 30 is completed.

4. The Superintending Engineer, Shimoga Circle ~~&~~ has recommende that the Sub Division may be continued till the end of June 1946 to complete the works in all respects. He further recommends that this period is necessary to complete the projects which are situated in out of the way places.

5.

C.O.,

5. Under the above circumstances, sanction of Government to the continuance of the Sub Division till the end of June 1948 at the first instance may kindly be obtained and communicated.

6. Pending sanction to the proposal, the establishment is being continued beyond the sanctioned period and the action taken may kindly be approved.

I have the honour to be,

Sir,

Your most obedient servant,

GCS/16th.

CHIEF ENGINEER FOR IRRIGATION.

3143
PW

G. R. S. App. F VI—G 2]

SUBJECT Continuance of the Special Sub Dn Constituted for Shimoga Kadalli and Gadina Kere Tank Works

6 copies

Diary No. of letter replied to.....

Section Est

File No. 80-46

Serial No. 2

General and Revenue Secretariat

( )

the 193 .

Proceedings of the Government of His Highness the Maharaja of Mysore.

Date of issue 3.2.47 193 .

Signed by Mr. BRR.

Read— GO No PW 65-24-27 dated 24-3-1944 sanctioning, inter-alia, the Constitution of a Sub division under an Asst Engineer, with the necessary establishment for a period of five years, for the execution of Shimoga Kadalli and Gadina Kere Projects in Shimoga Taluk.

2. Letter No 4335-7/E dated 17-12-1946 from the Chief Engineer for Irrigation, requesting sanction to the Continuance of the above Sub division, with the

May this be—

(i) printed ?

(ii) treated as a standing order ?

(iii) published in the Gazette, English Part ?

(vi) translated ?

(v) placed at the disposal of the press ?

(vi) published in the Gazette, Kannada Part ?

Order thereon.—No.

existing office and establishment
till the end of June 1948 to
enable the Bank Works being
Completed.
Order thereon No PW 4851-3 dated 3.2.47.

sanctioned, till the
end of June 1948.

Secy to Govt
PW Deptt

To

The CE to Govt and
the Comptroller of Accounts
the Audit Off & Exch Offr

List of Enclosure

24/1/47.

24/1/47

Copied by

Examined by

WD 0523—GPB—22,500—16-3-37

PROCEEDINGS OF THE GOVERNMENT OF HIS HIGHNESS THE MAHARAJA OF MYSORE

Public Works Departi

READ—

G.O.No.P.W.6524-27 dated 24-3-1944 sanctioning inter-alia, the constitution of a Sub Division, with the necessary establishment for a period of two years, for the execution of Thuppadahalli and Sokkahalla tank projects in Jagalur Taluk.

2. Letter No.4335-7/E dated 17-12-1946 from the Chief Engineer for Irrigation, requesting sanction to the continuance of the above Sub Division, with the existing officer and establishment till the end of June 1948 to enable the tank works being completed.

Order thereon No.P.W. 4851-3/Est 80-46-2 Dated Bangalore, 3-2-47

Sanctioned, till the end of June 1948.

Secretary to Government,
Public Works Department.

To

The Chief Engineer for Irrigation
The Comptroller of Mysore,
The Auditor, P.W.Department (through the FI.Sectt).

PROCEEDINGS OF THE GOVERNMENT OF HIS HIGHNESS THE MAHARAJA OF MYSORE

Public Works Department

READ—

G.O.No.P.W.6524-27 dated 24-3-1944 sanctioning inter-alia, the constitution of a Sub Division, with the necessary establishment for a period of two years, for the execution of Thuppadahalli and Sokkehalla tank projects in Jagalur Taluk.

2. Letter No.4335-7/E dated 17-12-1946 from the Chief Engineer for Irrigation, requesting sanction to the continuance of the above Sub Division, with the existing officer and establishment till the end of June 1948 to enable the tank works being completed.

Order thereon No.P.W.4951-3/Est 80-46-2 Dated Bangalore, 3-2-1947

Sanctioned, till the end of June 1948.

By Secretary to Government,
Public Works Department.

To

The Chief Engineer for Irrigation
The Comptroller of Mysore,
The Auditor, P.W.Department (through the FI.Sectt)

3143
PW

Appendix F. G.—1]

SUBJECT Continuance of the Special sub divisions Constructed for the Uruppadalli & Lokkedalla tank projects.

Section Est
File No. 80-46
Serial No. 3.

Diary No. of letter replied to.....

No. PW 4854

General and Revenue Secretariat

( )

the 194 .

To.

The Chief Engineer, Eastern Province
Batticaloa

Date of issue 3-2-47.

Sir

Signed by Mr. BRR

With reference to G.O. No. PW 4851-3/E-80-46-2 dated 3.2.47 sanctioning the continuance of the above sub divisions till the end of June 1948 I am directed to state that G.O.S observe that the progress secured by the said divisions is poor. I am therefore to request you kindly to investigate into the causes for the poor progress and to

List of enclosures.....

Copied by.....

Examined by.....

WD 02745—GPB—25,000—24-6-46

forward a request for the information of Govt.

2. Govt feel that constant supervision over these works is very necessary and that the officers in charge of these works require to be finished up.

3. I am also to request that all facilities may be given to the officers to enable them to get through the works early

Secret

Bou 27/4/42

Secy to Govt
PW Deptt

B 24/1/47

Secy 24/1/47

Est 80-46-4

Office of the Chief Engineer for
Irrigation in Mysore,
Dated Bangalore, 28th May 1947.

No. 8583/5
1 proposition Statement
in Duplicate
2 copies of letters
1 Statement
4.

29/5

To

The Secretary to Government,
Public Works Department,
Bangalore.

P.W. SECRETARIAT
6519
Date 30/5/47

Sir,

Continuance of the Special Sub Division constituted for the execution of Thuppadahally and Gadimakunte Tank works in Jagalur Taluk.

With reference to your letter No.P.W.4854/Est. 80-46-3 dated 3-2-1947, requesting to investigate into the causes for the poor progress on the above works and to forward a report for the information of Government, I have the honour to forward herewith a copy of letter No.2008 dated 20-4-1947 together with a copy of its enclosure received from the Superintending Engineer, Shimoga Circle which explains in detail the causes for short progress.

2. The Superintending Engineer, Shimoga Circle has recommended that two separate Sub Divisions may be constituted for the supervision of Thuppadahally and Gadimakunte Tank works so that undivided attention may be bestowed by the Assistant Engineer for the speedy completion of the works. The proposal of the Superintending Engineer, Shimoga Circle involves an extra cost of Rs.7,734/- per annum. He has further recommended, ~~that~~ with a view to overcoming the transport difficulties, the employment of 9 lorries with a quota of 150 gallons of petrol per lorry.

3. Under the above circumstances, sanction of Government to the formation of two separate Sub Divisions one at Thuppadahally and another at Gadimakunte with the establishment as provided in the proposition statement herein enclosed till the end of June 1948, may kindly be obtained and communicated.

I have the honour to be,
Sir,
Your most obedient servant,

GCS/28th.

CHIEF ENGINEER FOR IRRIGATION.

Annexure

Proposition statement of establishment of No.2 Irrigation Sub Division at Jagalur attached to the Irrigation Division, Chitaldrug.

Tank Works in the causes of Thuppadahalli & Gadimakunte Tank Works.

Present.					Proposed.				
No.	Designation.	Pay.	Average pay.	Total.	No.	Designation.	Grade pay.	Average cost.	Total.
	For Gadimakunte & Thuppadahally.					**For Thuppadahalli Tank works.**			
1	Asst. Engineer	200-40/2-400.	320	320	1	Asst. Engineer.	200-40/2-400	320	320
1	Overseer	80-5-125	108	108	1	Overseer	80-5-125	108	108
4	Surveyors.	35-5/2-80	58	232	2	Suboverseers	35-5/2-80	58	116
4	Peons.	11	11	44	2	Clerks	30-2-50-2-60	47½	95
2	Clerks.	30-3-45	41	82½	2	Peons.	11	11	22
	Construction allowance at 10% of pay.			79		Conveyance allowance to the Assistant Engineer, ~~xxx~~ Overseer and Suboverseers, at 32,24 and 15 respectively.			86.
	Conveyance allowance to the Assistant Engineer, Overseer, Surveyors at Rs.32, 24 and 15 respectively.		..	116.		Construction allo... ... 10% of pay.			66
	Total.			981½		Total.			813.
						For Gadimakunte Tank works.			
					1	Asst. Engineer.	200-40/2-400	320	320
					1	Overseer	80-5-125	108	108
					2	Suboverseers	35-5/2-80	58	116
					2	Clerks.	30-2-50-2-60	47½	95
					2	Peons.	11	11	22
						Construction allowance at 10% of pay.		...	66
						Conveyance allowance to Assistant Engineer, Overseer, and Suboverseers at Rs.32,24 and 15 respectively.		...	86.
						Total.			813.

Total cost per month is Rs.1,626 ~~per mensem.~~

Extra expense per month Rs.1,626 - 981½ = 644½

Proposition statement of establishment of No.2 Irrigation Sub Division Jagalur attached to the Irrigation Division, Chitaldrug.

Present.					Proposed.				
No.	Designation.	Pay.	Average pay.	Total.	No.	Designation.	Grade pay.	Average cost.	Total.
	For Gadinakunte & Thuppadahally.					For Thuppadahalli Tank works.			
1	Asst. Engineer	200-40/2-400.	320	320	1	Asst. Engineer.	200-40/2-400	320	320
1	Overseer	80-5-125	108	108	1	Overseer	80-5-125	108	108
4	Surveyors.	35-5/2-80	58	232	2	Suboverseers	35-5/2-80	58	116
1	Peons.	11	11	44	2	Clerks	30-2-50-2-60	47½	95
2	Clerks.	30-3-45	41½	82½	2	Peons.	11	11	22
	Construction allowance at 10% of pay.			79		Conveyance allowance to the Assistant Engineer, Overseer and Suboverseers, at 32,24 and 15 respectively.			86.
	Conveyance allowance to the Assistant Engineer, Overseer, Surveyors at Rs.32, 24 and 15 respectively.		..	116.		Construction allowance at 10% of pay.			66
	Total.			981½		Total.			813.
						For Gadinakunte Tank works.			
					1	Asst. Engineer.	200-40/2-400	320	320
					1	Overseer	80-5-125	108	108
					2	Suboverseers	35-5/2-80	58	116
					2	Clerks.	30-2-50-2-60	47½	95
					2	Peons.	11	11	22
						Construction allowance at 10% of pay.		...	66
						Conveyance allowance to Assistant Engineer, Overseer, and Suboverseers at Rs.32,24 and 15 respectively.		...	86.
						Total.			813.

Total cost per month is Rs.1,626 ~~per mensem~~

Extra expense per month Rs.1,626 - 981½ = 644½

Letter No.2008 dated 16/20th April 1947 from the Superintending Engineer, Shimoga Circle, to the Chief Engineer for Irrigation in Mysore, Bangalore.

Continuance of the Special Sub Division constituted for the execution of Thuppadahalli and Gadimakunte Tanks works in Jagalur Taluk.

With reference to your memo No.5642/E dated the 18th February 1947 forwarding a copy of Government Order No.P.W.4854/Est. 80-46-3 dated the 3rd February 1947, I have the honour to state that Government have observed that the progress on the work is poor and have requested that the causes for the poor progress may be investigated and a report submitted. Government have further observed that constant supervision over these works is very necessary and that officers in charge of these works require to be pulled up. They have further directed that all facilities may be given to officers to enable them to get through the works early.

2. A copy of letter No.497 dated the 4th March 1947 received from the Executive Engineer, Irrigation Division, Chitaldrug, is enclosed for kind perusal. This report explains at length the conditions obtaining the Tuppadahalli and Gadimakunte tanks. The chief cause for the poor progress is seen to be paucity of pieceworkers and labou for execution, and carts for conveyance of materials to the tank site The labour are mostly local labour and they desert the works for agricultural operations whenever the conditions for the latter are favourable. Carts required for transporting gravel, and stones etc., are mostly possessed by the Agricultural labour and these will be made available only when they are not needed on the fields.

With regard to supervision over these works, one Sub Division with an Assistant Engineer is sanctioned at present for both these tank works. Both are works of magnitude and the Assistant Engineer will have to be moving from Gadimakunte to Tuppadahally tank works very frequently for supervision and arranging payments. A close supervision can be achieved by having an independant Sub Division for each tank work. This will involve the entertainment of one Assistant Engineer, two Surveyors and two clerks.

The Executive Engineer has proposed with a view to overcome the transport difficulties, the employment of lorries with a quota of 150 gallons of petrol per lorry. The consolidation of bund is proposed to be speeded by means of Diesel powered rollers. In addition, trackways with Tip waggons are to be put up for rapid conveyance of gravel for the consolidation. It is reported by the Executive Engineer that the Irrigation Sub Division at Jagalur has only one serviceable lorry. Hence 9 more lorries, two Diesel Powered rollers and two miles of trolley track are needed for more speedy progress to be secured.

A statement showing the works that are yet to be done on these two tank works during the current year according to programme is enclosed. The collection of gravel to the extent of nearly 50,000 Cyds for Tuppadahalli and 77,800 Cyds of gravel for Gadimakunte has to be done. This cannot be transported with the small number of carts available, at these two places. Lorry transportation will improve the progress. It has not been possible to secure more lorries and the quantity of petrol issued by the Chief Rationing Authority is not adequate even for the existing lorries in the Division to work to the fullest extent.

The above conditions of execution prevailing at the two tank sites, the necessity for having two separate Sub Divisions and to have means of mechanical transport by lorries for stones etc., and track lines and tipping waggons for earthwork and gravel are brought to kind notice. The formation of a new Sub Division may be recommended to Government. In spite of all attempts made for lorries, track lines and tipping waggons, it has not beenpossible to secure them.

"COPY".

GCS/28th.

CHIEF ENGINEER FOR IRRIGATION.

Letter No.897 dated 4-3-1947 from the Executive Engineer, Irrigation Division, Chitaldrug, to the Superintending Engineer, Shimoga Circle, Shimoga.

With reference to your No.11312 dated 23-2-1947 calling for report regarding progress of Gadimakunte and Tuppadahally Tanks, I have the honour to invite your kind reference to this office No.535 dated 4-9-46 explaining the reasons for securing a low progress on these works and the facilities required to improve progress.

I am herewith enclosing the statement of major works done for the first half year and works to be done for the second half year. As can be seen that while normal progress has been secured in the case of Tuppadahalli tank, the progress has fallen down again in the case of Gadimakunte Tank. The reason for this is as already explained, the absence of regular pieceworkers in the locality who are depending upon contracts for profession.

In this locality labour has to be recruited from round about villages. As there was good rain fall, this year the local labour had sufficient work very near their houses. They required constant pressure to induce them to come to work. Unfortunately the one Surveyor that is working in that place fell constantly ill and was off and on leave for nearly three months. The Assistant Engineer who had to attend to Tuppadahalli tanks as well as this tank, did all he could do get as many labour as possible during this period. As he could not remain in the locality at all time, the labour was always dissipating specially since there was harvesting and preparing the lands due to late rains till the end of January 1947. The inability to encash P.A.sheets to pay the labour for want of sanction was also partly responsible for scaring away the labour as payments on Shandy days could not be arranged promptly for these days. This was counteracted to a certain extent by arranging to get P.A. amount from Parasurampur Sub Division for payments on Shandy days as was reported in this office No.D.C.794 dated 3-2-47.

To infuse confidence to the labour the Assistant Engineer was

29-8-1947 from the Chief Engineer for Irrigation, forwarding proposals for the formation of two separate Public Works Sub divisions, each under an Assistant Engineer and with necessary establishment, for the early completion of the Kuppadakalli and Gadimakunte (Sokkekalli) tank works.

Proposals Nos. Ph. 2317-19 Dated 26-8-47

Two estimates amounting to Rs 3.64 Lakhs and Rs 2.85 Lakhs were sanctioned in March 1944 for the Construction of tanks near Kuppadakalli and Gadimakunte (Sokkekalli) respectively in Jagalur Taluk. At the time of sanctioning these estimates the Chief Engineer proposed the formation of two separate sub divisions for the execution of these two tank works. However, only one sub division was sanctioned, as Govt considered that the two works are in one and the same basin and that one sub division would be sufficient.

List of Enclosures

Copied by

Examined by

was on the works practically every day from the 20th December to middle of January 1947 getting the works done and payments made on rolls etc. This has to a certain extent infused confidence in the labour and the strength of labour has increased gradually from 70 to 200. In the course of a fortnight it is expected to get to 400. All these are being maintained departmentally for want of piece-workers who would get works from these.

In this locality all the carts are owned by ryots and very few own carts to live by hire. So far carts could not be induced to come to work though they have been offered Rs.2-8-0 per day for 8 hours of work. As the harvesting is complete and the cotton harvesting is to commence, all the local carts owned by ryots will be engaged in transporting the grains, fodder and cotton from the fields to their houses and from their house to market. Even the few that own carts earn Rs.3-8-0 per day for works which does not involve heavy manual labour. To engage the 400 labourers that are expected to come for work, transport facility is required as the materials ar to be carted from distance of about a furlong and it is uneconomical to engage labour for transport by head load. Therefore we require at least 6 lorries with 750 gallons of petrol per month to complete the earthwork to be done in the gap portion where the major portion of the work is to be done as per programme of 1946-47. These 6 ~~lorr~~ lorries are required as we have to complete the gap portion before the end of April to prevent damage or overflow. By making one Steam Road Roller for consolidating this gap portion it would greatly facilitate rapid work.

Regarding Tuppadahalli tank, we have to work in the gap portion as the flanks have all come to about to the approved level for this year's programme. Even there due to late rains the valley portion could be commenced early. In the usual course rain should have stopped by about the end of October and working season commenced from November 1946. That is now put off this year to end of January 1947. Extension of the central puddle core wall is being done now and will be completed before the middle of next month as it is to be done in

in short bits due to heavy percolation. To complete bank work in this gap portion to required level, we have to supplement the conveyance of materials by the carts and buffellos now working here. New puddle and gravel are being collected at the gap portion to commence the puddle work immediately the puddle trench is clear. Out of the 45,000 Cyds of earthwork to be done in this portion nearly 15,000 Cyds can be expected to be done by other conveyance. Of this 20,000 Cyds is for gap portion. This work is to be finished in 60 working days. So 300 Cyds have to be worked every day at 60 Cyds per lorry per day. Five lorries with 500 gallons of petrol per month is needed.

As the maximum strength of labour can be expected to work between March and April 1947, these lorries with petrol may kindly be arranged to be spared in almost a week's time to take full advantage of the situation.

"COPY"

GCS/28th. CHIEF ENGINEER FOR IRRIGATION.

Statement of works done on Tuppadahalli and Gadimakunte Tank works.

Item of work.	Progress to be achieved for 46-47 as per programme. Cyds.	Progress secured during the half year. Cyds.	Balance for the second half year. Cyds.	Remarks.
		TUPPADAHALLI.		
Earthen bank.	66,000	22,000	45,000	
Puddle corewall	8,863	4,000	4,500	
Revetment	2,706	1,000	1,706.	
		GADIMAKUNTE.		
Earthen bank.	74,000	10,000	64,000	
Puddle corewall	12,000	2,800	9,000	
Revetment	4,800		4,800	Stones to the extent of 1000 Cyds is collected at site.

"COPY"

GCS/28th.

CHIEF ENGINEER FOR IRRIGATION.

6519 PW

G. R. S. App. F VI—G. 2]

SUBJECT Formation of two separate PW Sub Divisions for the Execution of Hanspadadalli and Gadimakunte Tank works in Tayalur Taluk

Diary No. of letter replied to.....

Section. Est-

File No. 80-4-

Serial No. 5.

General and Revenue Secretariat.

( )

the 194

Proceedings of the Government of His Highness the Maharaja of Mysore.

Date of issue 26-8- 194/

Signed by Mr HPS

Read— G O No PW 6524-27 dated 24-3-1944 sanctioning inter-alia the Constitution of a sub division under an Asst Engineer with the necessary establishment for a period of two years for the execution of Hanspadadalli and Lokkedalla (Gadimakunte) tank project in Tayalur Taluk.

Order thereon.—No.

2. G O No PW 4851-3/Est 80-46-2 dated 3-2-1947, sanctioning the continuance of the above sub division, with the existing office and establishment till the end of June 1948

3. Letter No. PW 8583/E dated

May this be—

(i) printed ?

(ii) treated as a Standing Order ?

(iii) published in the Gazette, English Part ?

(iv) translated ?

(v) placed at the disposal of the Press ?

(iv) published in the Gazette, Kannada Part ?

6 20/8/47

G. R. S. App. F. G. 3.

GENERAL AND REVENUE SECRETARIAT.

(*Continuation sheet draft form.*)

2. 2nd January 1947

Govt observed that the progress on the above two works was very poor. In fact upto end of October 1946 only an outlay of Rs 88,062/- and Rs 68,824/- had been incurred leaving a heavy balance of Rs 275,938/- and Rs 2,16,179/- respectively. The Chief Engineer for Irrigation, who was requested to give reasons for the poor progress, has forwarded proposals for the formation of two separate sub divisions, each under an Assistant Engineer with the establishments as shown in the annexure, till the end of June 1948. In lieu of the existing single sub division, so each work may be in independent charge of each sub division officer.

3. Work on the works

Maj J.

6519

are in one and the same Taluk
the distance between the places
is very nearly 30 miles and it is
not possible for one Assistant Engr
to effectively supervise both the
works. In the circumstances
Govt are pleased to sanction
the proposals of the Chief Engr
till the end of June 1948, the
cost being debited to the respective
estimates for the Tank works

Pos c 19.8.47 HPS
Secy to Govt. 19.8.47
P.W. Dept

To

The CE for Irrigation
The Superintending Engr } Trichy & Salem
The Executive Engr

B 18/8/47. 2 Spare Copies
hrs 19/8/47

PROCEEDINGS OF THE GOVERNMENT OF HIS HIGHNESS THE MAHARAJA OF MYSORE

Public Works Department

READ —

Government Order No.P.W.6884-47 dated 24-8-1944 sanctioning, inter-alia, the constitution of a Sub Division under an Assistant Engineer with the necessary establishment for a period of two years for the execution of Bhupasandrahalli and Gokkohalla (Gudimakunte) tank projects in Jagalur Taluk.

2. Government Order No.P.W.4851-3/Est.80-46-2 dated 5-4-1947, sanctioning the continuance of the above Sub Division, with the existing Officer and establishment, till the end of June 1948.

3. Letter No.8583/3. dated 20-5-1947 from the Chief Engineer for Irrigation, forwarding proposals for the formation of two separate Public Works Sub Divisions, each under an Assistant Engineer and with necessary establishment for the early completion of the Bhupasandrahalli and Gudimakunte (Gokkohalli) tank works.

ORDER (P) No. 2317-19/Est-80-46-5

Dated Bangalore 26 August 1947.

The estimates amounting to Rs.3.64 lakhs and Rs.4.82 lakhs were sanctioned in Dec 1944 for the construction of Bhupasandrahalli and Gudimakunte (Gokkohalli) respectively in Jagalur Taluk. At the time of sanctioning the estimates, the Chief Engineer proposed the formation of two separate Sub-Divisions for the execution of these two tank works. However only one sub-division was sanctioned, the Government considering that the two works are in one taluk and that one sub-division would be sufficient.

2. In January 1947 Government observed that there was no progress on the above two works for very long. In fact, upto the end of October 1946 only Rs.10,688/- and Rs.25,312/- had been incurred leaving a heavy balance of Rs.2,75,338/- and Rs.3,16,175/- respectively. The Chief Engineer for Irrigation, who was requested to investigate into the cause for poor progress, has forwarded proposals for the formation of two separate sub-divisions, each under an Assistant Engineer with the establishment shown in the annexure, till the end of June 1948 in lieu of the existing single sub division, so that each work may be an independent charge of each Sub Division Officer.

3. Though both the works are in one taluk, the distance between the places is very nearly 60 miles and it is not possible for one Assistant Engineer to effectively supervise both the works. In the circumstances, Government are pleased to sanction the proposals of the Chief Engineer till the end of June 1948, the cost being debited to the respective estimates for the two works.

H. Puttaswamy 22.8.47

Secretary to Government,
Public Works Department.

To

The Chief Engineer for Irrigation,
The Controller to Government,
The Auditor, Public Works Deptt.,
} through financial Secretariat.

ANNEXURE A.

Establishment sanctioned for the construction of Thuppadahalli & Gadimakunte Tank Works.

No.	Present. Designation.	Pay.	Average pay.	Total.	No.	Proposed. Designation.	Grade pay.	Average cost.	Total.
	For Gadimakunte & Thuppadahally.					**For Thuppadahalli Tank Works.**			
1.	Asst. Engineer	200-40/2-400	320	320	1	Asst. Engineer.	200-40/2-400	320	320
1	Overseer	80-5-125	108	108	1	Overseer	80-5-125	108	108
4	Surveyors	35-5/2-8	58	232	2	Subovorseers.	35-5/2-80	58	116
4	Peons	11	11	44	2	Clerks	30-2-50-2-60	47½	95
2	Clerks	30-3-45	41½	82½	2	Peons	11	11	22
	Construction allowance at 10% of pay			79		Conveyance allowance to the Assistant Engineer, Overseer and Subovorseers. at 32,24 and 15 respectively.			86
	Conveyance allowance to the Assistant Engineer, Overseer, Surveyors at Rs.32, 24, and 15 respectively.		...	116		Construction allowance at 10% of pay.			66
			Total	981½				Total	813
						For Gadimakunte Tank Works.			
					1	Asst. Engineer.	200-40/2-400	320	320
					1	Overseer	80-5-125	108	108
					2	Subovorseers	35-5/2-80	58	116
					2	Clerks	30-2-50-2-60	47½	95
					2	Peons	11	11	22
						Construction allowance at 10% of pay.		...	66
						Conveyance allowance to Assistant Engineer, Overseer, and Subovorseers at Rs.32,24 and 15 respectively.		...	86
								Total.	813

Total cost per month is Rs.1,626.
Extra expense per month Rs.1,626 - 981½ = 644½
Extra cost per year is 644½ x 12 = 7,734

H. Pattuswamy 22.8.49
Secretary to Government, P.W.D.

PROCEEDINGS OF THE GOVERNMENT OF HIS HIGHNESS THE MAHARAJA OF MYSORE

Public Works Depa.....

READ —

Government Order No.P.W.6584-27 dated 24-3-1944 sanctioning, inter-alia, the constitution of a Sub Division under an Assistant Engineer with the necessary establishment for a period of two years for the execution of Thuppadahalli and Sokkehalla (Gadimakunte) tank projects in Jagalur Taluk.

2. Government Order No.P.W.4851-3/Est.80-46-2 dated 3-8-1947, sanctioning the continuance of the above Sub Division, with the existing Officer and establishment, till the end of June 1948.

3. Letter No.8583/2. dated 29-5-1947 from the Chief Engineer for Irrigation, forwarding proposals for the formation of two separate Public Works Sub Divisions, each under an Assistant Engineer and with necessary establishment for the early completion of the Thuppadahalli and Gadimakunte (Sokkehalli) tank works.

CHIEF E... CH No.P.J. 2317-19/Est 80-46-5

Dated Bangalore 26 August 1947.

Two estimates amounting to Rs.3.64 lakhs and Rs.2.80 lakhs were sanctioned in March 1944 for the construction of tanks near Thuppadahalli and Gadimakunte (Sokkehalli) respectively in Jagalur Taluk. At the time of sanctioning these estimates, the Chief Engineer proposed the formation of two separate Sub-Divisions for the execution of these two tank works. However only one sub division was sanctioned, as Government considered that the two works are in one and the same taluk and that one sub division would be sufficient.

2. In January 1947 Government observed that the progress on the above two works was very poor. In fact, up to end of October 1946 only an outlay of Rs.85,062/- and Rs.63,821/- had been incurred leaving a heavy balance of Rs.2,75,938/- and Rs.2,16,179/- respectively. The Chief Engineer for Irrigation, who was requested to investigate into the cause for poor progress, has forwarded proposals for the formation of two separate sub-divisions, each under an Assistant Engineer with the establishment as shown in the annexure, till the end of June 1948 in lieu of the existing single sub division, so that each work may be in independent charge of each Sub Division Officer.

3. Though both the works are in one taluk, the distance between the places is very nearly 30 miles and it is not possible for one Assistant Engineer to effectively supervise both the works. In the circumstances, Government are pleased to sanction the proposals of the Chief Engineer till the end of June 1948, the cost being debited to the respective estimates for the tank works.

S. Puttaswamy 22.8.47

Secretary to Government,
Public Works Department.

To

The Chief Engineer for Irrigation,
The Comptroller to Government,
The Auditor, Public Works Deptt.,

through Financial Secretariat.

ANNEXURE.

Establishment sanctioned for the construction of Thuppadahalli & Gadimakunte Tank works.

	Present.				Proposed.			
No.	Designation.	Pay.	Average pay.	Total.	No.	Designation.	Grade pay.	Average cost.	Total.
	For Gadimakunte & Thuppadahally.					**For Thuppadahalli Tank Works.**			
1.	Asst. Engineer	200-40/2-400	320	320	1	Asst. Engineer.	200-40/2-400	320	320
1	Overseer	80-5-125	108	108	1	Overseer	80-5-125	108	108
4	Surveyors	35-5/2-80	58	232	2	Subovorseers.	35-5/2-80	58	116
4	Peons	11	11	44	2	Clerks	30-2-50-2-60	47½	95
2	Clerks	30-3-45	41½	82½	2	Peons	11	11	22
	nstruction allowance at 10% of pay			79		Conveyance allowance to the Assistant Engineer, Overseer and Suboverseers, at 32,24 and 15 respectively.			86
	nveyance allowance to the Assistant ineer, Overseer, Surveyors at Rs.32, , and 15 respectively.		...	116		Construction allowance at 10% of pay.			66
			Total	981½				Total	813
						For Gadimakunte Tank works.			
					1	Asst. Engineer.	200-40/2-400	320	320
					1	Overseer	80-5-125	108	108
					2	Suboverseers	35-5/2-80	58	116
					2	Clerks	30-2-50-2-60	47½	95
					2	Peons	11	11	22
						Construction allowance at 10% of pay.		...	66
						Conveyance allowance to Assistant Engineer, Overseer, and Suboverseers at Rs.32,24 and 15 respectively.			86
								Total.	813

Total cost per month is Rs.1,626.
Extra expense per month Rs.1,626 - 981½ = 644½
Extra cost per year is 644½ x 12 = 7,734.

P. Pattaswamy 22.8.47
for Secretary to Government, P.W.D.
